



ID	Task Name	Duration	Start	Finish	Predecessors	2022	Qtr 2, 2022	Qtr 3, 2022	Qtr 4, 2022	Qtr 1, 2023	
						Mar	Apr	May	Jun	Jul	Aug
1	Heritage Move Micro Schedule	175 days	Mon 4/18/22	Fri 12/16/22							
2	Schedule update	0 days	Mon 4/18/22	Mon 4/18/22							
3	Completion of documents to be sent for Heritage Perm	62 days	Mon 4/18/22	Wed 7/13/22							
4	Completion of a Heritage Conservation Plan for the "preferred option"	7 days	Mon 4/18/22	Tue 4/26/22	2						
5	Submission of a formal application for a heritage permit with Heritage Conservation Plan	0 days	Tue 4/26/22	Tue 4/26/22	4						
6	City Staff Report	0 days	Wed 4/27/22	Wed 4/27/22	5						
7	BHSC Review (June 10th or June 20th) city to confirm	0 days	Mon 6/20/22	Mon 6/20/22	6						
8	City council to review	0 days	Wed 7/13/22	Wed 7/13/22	7						
9	Staff review of "deemed complete" application and City Council decision (90 days)	40 days	Wed 4/27/22	Tue 6/21/22	5						
10	Design requirements for Heritage Building move	13 days	Mon 4/18/22	Wed 5/4/22							
11	Engineering and pricing for Temp shoring system for Building move (Mar	13 days	Mon 4/18/22	Wed 5/4/22	2						
12	Engineering and pricing for temporary structural steel for the Heritage building (J.Cook)	13 days	Mon 4/18/22	Wed 5/4/22	2						
13	Engineering and pricing for structural steel to raise the Heritage Building (J.Cook)	13 days	Mon 4/18/22	Wed 5/4/22	2						
14	Civil Engineering and pricing for the temporary road for Heritage Building move. (Pattersen)	13 days	Mon 4/18/22	Wed 5/4/22	2						
15	Finalize pricing and approvals	67 days	Mon 4/18/22	Tue 7/19/22							
16	Compile pricing for complete scope for heritage works	3 days	Thu 5/5/22	Mon 5/9/22	11,12,13,14						
17	Reliance / CF contract	21 days	Mon 4/18/22	Mon 5/16/22	2						
18	Submit and approve for building move	5 days	Tue 5/10/22	Mon 5/16/22	16						
19	Award Scopes	1 day	Tue 5/17/22	Tue 5/17/22	18						
20	Procure Steel	45 days	Wed 5/18/22	Tue 7/19/22	19						
21	Permits / City approvals	47 days	Mon 4/18/22	Tue 6/21/22							

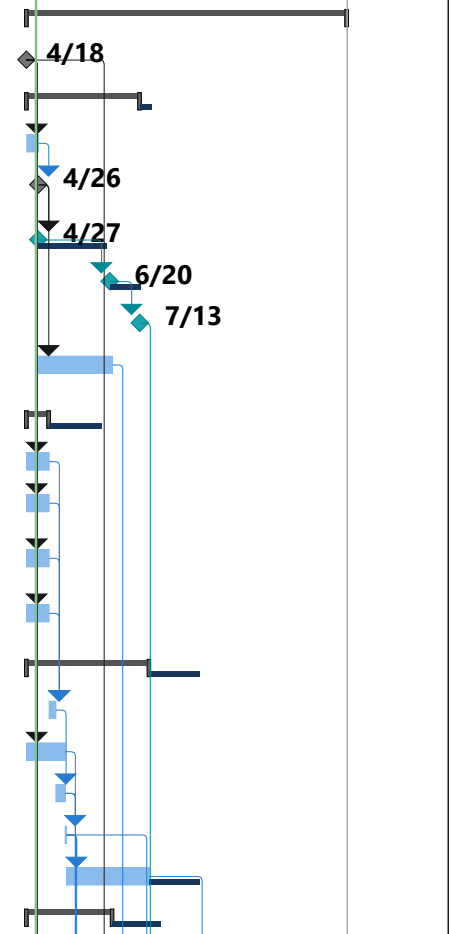

Project: Detailed Heritage Move
Date: Mon 4/25/22

Task		Manual Task		Deadline	
Split		Duration-only		Critical	
Milestone		Manual Summary Rollup		Critical Split	
Summary		Manual Summary		Progress	
Project Summary		Start-only		Manual Progress	
Inactive Task		Finish-only		Slack	
Inactive Milestone		External Tasks			
Inactive Summary		External Milestone			


ID	Task Name	Duration	Start	Finish	Predecessors	022	Qtr 2, 2022	Qtr 3, 2022	Qtr 4, 2022	Qtr 1, 2023	
						Mar	Apr	May	Jun	Jul	Aug
22	Tree Permit required (CF)	20 days	Mon 4/18/22	Fri 5/13/22	2						
23	Heritage Permit to move heritage components (CF)	0 days	Tue 6/21/22	Tue 6/21/22	2,9						
24	Storm line Cut and Cap (Reliance)	25 days	Mon 4/18/22	Fri 5/20/22	2						
25	Sanitary line cut and cap (Reliance)	30 days	Mon 4/18/22	Fri 5/27/22	2						
26	Power disconnect (Reliance)	30 days	Mon 4/18/22	Fri 5/27/22	2						
27	Disconnect water (Reliance)	30 days	Mon 4/18/22	Fri 5/27/22	2						
28	Nicholas lane closure permits from the city (Reliance)	30 days	Mon 4/18/22	Fri 5/27/22	2						
29	Gas disconnect and relocate (S&A, Reliance, Landscaping)	30 days	Mon 4/18/22	Fri 5/27/22	2						
30	Mobilize for Heritage Building Move	154 days	Tue 5/17/22	Fri 12/16/22							
31	Civil scope for Heritage Building Move	154 days	Tue 5/17/22	Fri 12/16/22							
32	Mobilize and set up site	5 days	Tue 5/17/22	Mon 5/23/22	18,17						
33	Locates for site services	3 days	Thu 5/19/22	Mon 5/23/22	19,22,32FF						
34	Clear and grade site for building move	3 days	Mon 5/30/22	Wed 6/1/22	33,24,22,25,26,27,2						
35	Prep Heritage building as per city's approval	12 days	Wed 7/13/22	Thu 7/28/22	34,25,26,27,8						
36	Remove front door and glass	3 days	Fri 7/29/22	Tue 8/2/22	35,23						
37	Install lateral bracing and supports on exterior	3 days	Wed 8/3/22	Fri 8/5/22	36						
38	Remove heritage stones as required for exterior	3 days	Wed 8/3/22	Fri 8/5/22	37FF						
39	Install lateral bracing for interior walls	3 days	Mon 8/8/22	Wed 8/10/22	38						
40	Remove flag stones and front door as required / weekend work as we	12 days	Thu 8/11/22	Fri 8/26/22	39						
41	Install W210's	15 days	Mon 8/29/22	Fri 9/16/22	40,20						
42	Remove heritage stones for W210's	15 days	Mon 8/29/22	Fri 9/16/22	41FF						
43	Install W250 cross beams	10 days	Mon 9/19/22	Fri 9/30/22	42						

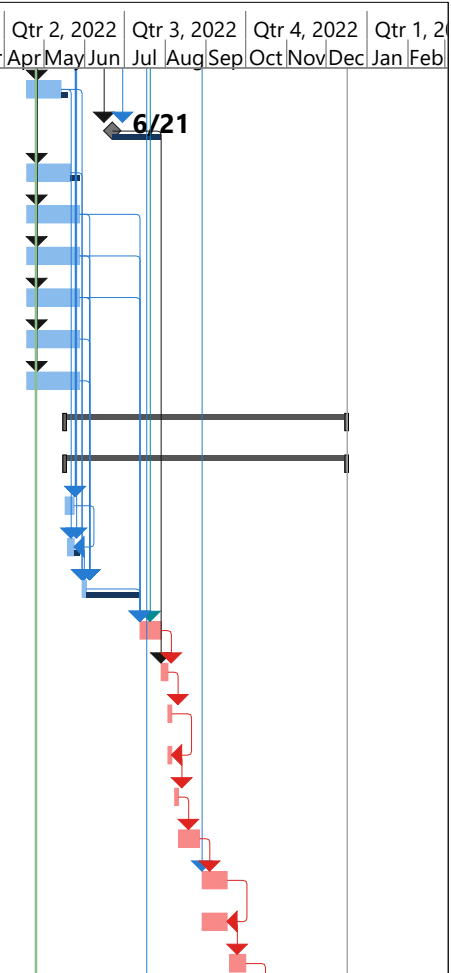

Project: Detailed Heritage Move
Date: Mon 4/25/22

Task		Manual Task		Deadline	
Split		Duration-only		Critical	
Milestone		Manual Summary Rollup		Critical Split	
Summary		Manual Summary		Progress	
Project Summary		Start-only		Manual Progress	
Inactive Task		Finish-only		Slack	
Inactive Milestone		External Tasks			
Inactive Summary		External Milestone			

ID	Task Name	Duration	Start	Finish	Predecessors	022	Qtr 2, 2022	Qtr 3, 2022	Qtr 4, 2022	Qtr 1, 2023	
						Mar	Apr	May	Jun	Jul	Aug
44	Remove Heritage Masonry to accommodate W250 beams	10 days	Mon 9/19/22	Fri 9/30/22	43FF						
45	Install needle beams	10 days	Mon 10/3/22	Fri 10/14/22	44						
46	Remove Heritage stones for Needle beams	10 days	Mon 10/3/22	Fri 10/14/22	45FF						
47	Install Steel supports for Barrel Vaults	10 days	Mon 10/17/22	Fri 10/28/22	46						
48	Remove Heritage masonry for barrel Vaults	10 days	Mon 10/17/22	Fri 10/28/22	47FF						
49	Complete civil components to accommodate building move	10 days	Mon 7/18/22	Fri 7/29/22	19						
50	Install 20 piles	20 days	Mon 8/1/22	Fri 8/26/22	49						
51	Excavate to sound substrate for temp road	5 days	Mon 8/29/22	Fri 9/2/22	50						
52	Backfill engineered fill for temp road	5 days	Mon 9/5/22	Fri 9/9/22	51						
53	Prep for building move and move building	18 days	Mon 10/31/22	Wed 11/23/22	52,47,48						
54	Weld building in final location	2 days	Thu 11/24/22	Fri 11/25/22	53						
55	Demobilize for building movers	10 days	Mon 11/28/22	Fri 12/9/22	54						
56	Prepare Heritage building for remainder of site works	5 days	Mon 12/12/22	Fri 12/16/22	55						
57	Complete	0 days	Fri 12/16/22	Fri 12/16/22	56FF						

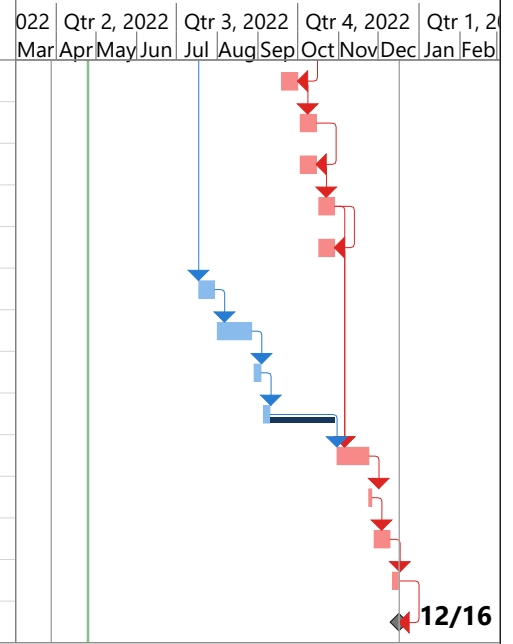

Project: Detailed Heritage Move
Date: Mon 4/25/22

Task		Manual Task		Deadline	
Split		Duration-only		Critical	
Milestone		Manual Summary Rollup		Critical Split	
Summary		Manual Summary		Progress	
Project Summary		Start-only		Manual Progress	
Inactive Task		Finish-only		Slack	
Inactive Milestone		External Tasks			
Inactive Summary		External Milestone			
