


LEGEND

---	PROPERTY LINE
- - - - -	PROPOSED LIMIT OF UNDERGROUND PARKING
- - - - -	PROPOSED LIMIT OF BUILDING OVERHANG
---	PROPOSED CURB
DC	PROPOSED DEPRESSED CURB
•••••	PROPOSED BOLLARDS
---	PROPOSED TRENCH DRAIN
▼	PROPOSED BUILDING ENTRANCE
○	PROPOSED FILTER BAGS AT CATCHBASINS AND CATCHBASIN MANHOLES
MM	PROPOSED MUD MAT
---	LIGHT DUTY SILT FENCE (OPSD 219.110)
DC	EXISTING DEPRESSED CURB
HT	EXISTING HYDRO TRANSFORMER
BL	EXISTING BOLLARD
EX LS	EXISTING LAMP POST
EX CB	EXISTING CATCH BASIN
STMMH	EXISTING STORM MANHOLE
---	EXISTING TREES / VEGETATION
---	EXISTING CURB
EX UP	EXISTING UTILITY POLE C/W GUY WIRES
---	EXISTING FENCE

- EROSION AND SEDIMENT CONTROL NOTES:**
- 1) ALL EROSION AND SEDIMENT CONTROLS ARE TO BE INSTALLED TO THE SATISFACTION OF THE ENGINEER AND THE CITY OF OTTAWA. THEY ARE TO BE APPROPRIATE TO THE SITE CONDITIONS, PRIOR TO UNDERTAKING ANY SITE ALTERATIONS (FILLING, GRADING, REMOVAL OF VEGETATION, ETC.) AND DURING ALL PHASES OF SITE PREPARATION AND CONSTRUCTION. THESE PRACTICES ARE TO BE IMPLEMENTED IN ACCORDANCE WITH THE CURRENT BEST MANAGEMENT PRACTICES FOR EROSION AND SEDIMENT CONTROL AND SHOULD INCLUDE AS A MINIMUM THOSE MEASURES INDICATED ON THE PLAN.
 - 2) TO PREVENT SURFACE EROSION FROM ENTERING THE DITCH OR STORM SYSTEM DURING CONSTRUCTION, FILTER CLOTH WILL BE PLACED UNDER GRATES OF CATCHBASINS AND STRUCTURES. A LIGHT DUTY SILT FENCE BARRIER WILL ALSO BE INSTALLED ALONG THE PROPERTY LINES. THESE CONTROL MEASURES WILL REMAIN IN PLACE UNTIL VEGETATION HAS BEEN ESTABLISHED AND CONSTRUCTION IS COMPLETE.
 - 3) THE SEDIMENT CONTROL MEASURES SHALL ONLY BE REMOVED WHEN, IN THE OPINION OF THE ENGINEER, THE MEASURES ARE NO LONGER REQUIRED. NO CONTROL MEASURES MAY BE PERMANENTLY REMOVED WITHOUT PRIOR AUTHORIZATION FROM THE ENGINEER.
 - 4) THE CONTRACTOR SHALL IMMEDIATELY REPORT TO THE ENGINEER ANY ACCIDENTAL DISCHARGES OF SEDIMENT MATERIAL INTO ANY DITCH OR STORM SEWER SYSTEM. APPROPRIATE RESPONSE MEASURES, INCLUDING ANY REPAIRS TO EXISTING CONTROL MEASURES OR THE IMPLEMENTATION OF ADDITIONAL CONTROL MEASURES, SHALL BE CARRIED OUT BY THE CONTRACTOR WITHOUT DELAY.
 - 5) THE CONTRACTOR ACKNOWLEDGES THAT FAILURE TO IMPLEMENT EROSION AND SEDIMENT CONTROL MEASURES MAY BE SUBJECT TO PENALTIES IMPOSED BY ANY APPLICABLE REGULATORY AGENCY.
 - 6) ROADWAYS ARE TO BE SWEEP AS REQUIRED OR AS DIRECTED BY THE ENGINEER AND/OR MUNICIPALITY.
 - 7) THE CONTRACTOR SHALL ENSURE PROPER DUST CONTROL IS PROVIDED WITH THE APPLICATION OF WATER (AND IF REQUIRED, CALCIUM CHLORIDE) DURING DRY PERIODS.

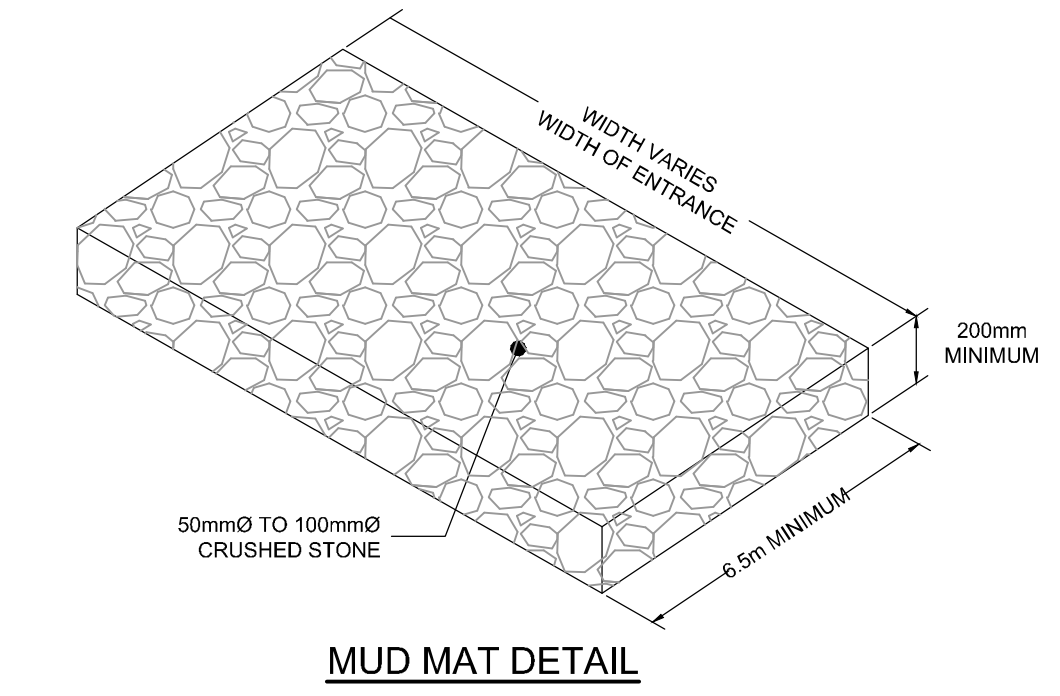


Andrew McCreight
ANDREW MCCREIGHT
 MANAGER (A), DEVELOPMENT REVIEW CENTRAL
 PLANNING, REAL ESTATE & ECONOMIC DEVELOPMENT
 DEPARTMENT, CITY OF OTTAWA

APPROVED
 By Andrew McCreight at 3:25 pm, Sep 15, 2022

**NOT FOR
 CONSTRUCTION**


NOTE:
 THE POSITION OF ALL POLE LINES, CONDUITS,
 WATERMANS, SEWERS AND OTHER
 UNDERGROUND AND OVERGROUND UTILITIES AND
 STRUCTURES IS NOT NECESSARILY SHOWN ON
 THE CONTRACT DRAWINGS, AND WHERE SHOWN,
 THE ACCURACY OF THE POSITION OF SUCH
 UTILITIES AND STRUCTURES IS NOT GUARANTEED.
 BEFORE STARTING WORK, DETERMINE THE EXACT
 LOCATION OF ALL SUCH UTILITIES AND
 STRUCTURES AND ASSUME ALL LIABILITY FOR
 DAMAGE TO THEM.

CLARIDGE HOMES
 CLARIDGE HOMES
 SUITE 2001,
 210 GLADSTONE AVENUE,
 OTTAWA, ONTARIO
 K2P 0Y6.



NOTE:
 CONTRACTOR TO CONFIRM ELEVATIONS OF INFRASTRUCTURE IN THE STREET
 PRIOR TO EXTENDING SERVICES INTO THE SITE AND SHALL NOTIFY ENGINEER OF
 ANY DISCREPANCIES IMMEDIATELY.

No.	REVISION	DATE	BY
1.	XXXX	JAN1/10	XXX

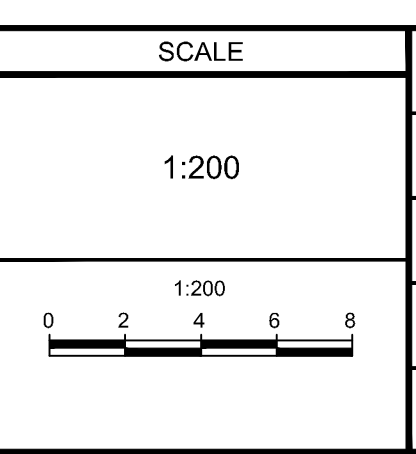

FOR REVIEW ONLY
DESIGN: C/JF
CHECKED: ARM
DRAWN: C/JF
CHECKED: ARM
APPROVED: GJM

NOVATECH
 Engineers, Planners & Landscape Architects
 Suite 200, 240 Michael Cowland Drive
 Ottawa, Ontario, Canada K2M 1P6
 Telephone: (613) 254-9643
 Facsimile: (613) 254-5867
 Website: www.novatech-eng.com

LOCATION CITY OF OTTAWA 1040 SOMERSET STREET WEST	PROJECT No. 112191-01
DRAWING NAME EROSION AND SEDIMENT CONTROL PLAN	REV # 1
DRAWING No. 112191-ESC	
