
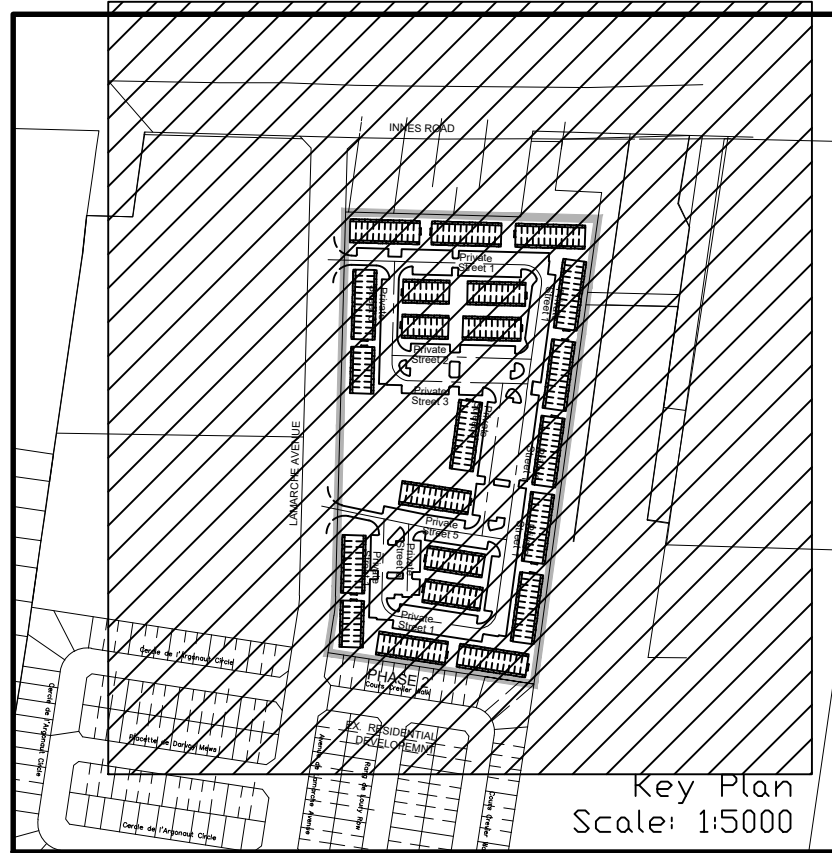


*John Seigny*  
**JOHN SEIGNY C.E.T.**  
**MANAGER (A), DEVELOPMENT REVIEW EAST**  
**PLANNING, DEVELOPMENT & BUILDING SERVICES**  
**DEPARTMENT, CITY OF OTTAWA**

**APPROVED**  
By sevignyjo at 12:43 pm, Sep 11, 2025

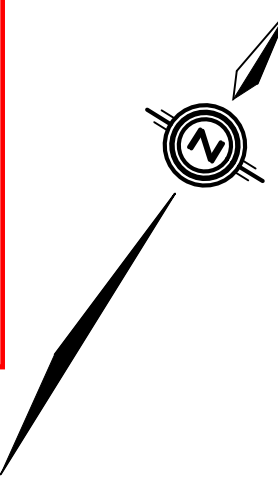

**MONITORING OF SEDIMENT AND EROSION CONTROLS**  
MONITORING AND REPORTING TO BE COMPLETED IN ACCORDANCE WITH THE MINISTRY OF THE ENVIRONMENT, CONSERVATION, AND PARKS (MECP) AND CONSERVATION AUTHORITY REGULATIONS.

**MAINTENANCE PROGRAM**  
ALL DAMAGED ESO MEASURES SHOULD BE REPAIRED AND/OR REPLACEMENT WITHIN 48 HOURS OF THE INSPECTION.  
THE ENVIRONMENTAL MONITOR IS REQUIRED TO SUBMIT UPDATES TO THE CITY/ REGION/ CONSERVATION AUTHORITY BY EMAIL IN A TIMELY MANNER.  
SEDIMENT SHOULD BE REMOVED FROM THE SEDIMENT CONTROL FENCING ONCE SEDIMENT HAS ACCUMULATED TO A LEVEL OF ONE-THIRD THE HEIGHT OF FENCING OR TO A HEIGHT OF 30 cm. ANY AMOUNT OF ACCUMULATED SEDIMENT SHOULD BE REMOVED PRIOR TO THE REMOVAL OF THE CONTROL MEASURES.

**SEQUENCE OF ACTIVITIES**  
THE EROSION AND SEDIMENT CONTROL MEASURES MUST BE INSTALLED IN ACCORDANCE WITH THE FOLLOWING SEQUENCE:  
- INSTALLATION OF THE SEDIMENT CONTROL FENCING WHERE INDICATED.  
- REMOVAL OF SITE VEGETATION IN ACCORDANCE WITH ALL APPLICABLE BY-LAWS.  
- REGULAR MONITORING OF THE SEDIMENT CONTROL FENCES BY THE CONTRACTOR TO VERIFY THAT THE FENCES ARE FUNCTIONING AS INTENDED.  
- REMOVAL OF THE EROSION AND SEDIMENT CONTROL DEVICES ONCE THE SITE HAS BEEN STABILIZED.

**SPILLS CONTROL NOTES**  
ALL CONSTRUCTION EQUIPMENT SHALL BE REFUELED, MAINTAINED AND STORED NO LESS THAN 30 METERS FROM THE WATERCOURSES, STREAMS, CREEKS, WOOLLOTS AND ANY ENVIRONMENTALLY SENSITIVE AREAS, OR AS OTHERWISE SPECIFIED.  
THE CONTRACTOR MUST IMPLEMENT ALL NECESSARY MEASURES IN ORDER TO PREVENT LEAKS, DISCHARGES OR SPILLS OF POLLUTANTS, DELETERIOUS MATERIALS, OR OTHER SUCH MATERIALS OR SUBSTANCES WHICH WOULD OR COULD CAUSE AN ADVERSE IMPACT TO THE NATURAL ENVIRONMENT.  
IN THE EVENT OF A LEAK, DISCHARGE OR SPILL OF A POLLUTANT, DELETERIOUS MATERIAL OR OTHER SUCH MATERIAL OR SUBSTANCE WHICH WOULD OR COULD CAUSE AN ADVERSE IMPACT TO THE NATURAL ENVIRONMENT, THE CONTRACTOR SHALL,  
1. IMMEDIATELY NOTIFY THE APPROPRIATE FEDERAL, PROVINCIAL AND LOCAL GOVERNMENT MINISTRIES, DEPARTMENTS, AGENCIES AND AUTHORITIES OF THE INCIDENT IN ACCORDANCE WITH ALL CURRENT LAWS, LEGISLATION, ACTS, BY-LAWS, PERMITS, APPROVALS, ETC.  
2. TAKE IMMEDIATE MEASURES TO CONTAIN THE MATERIAL OR SUBSTANCE, AND TO TAKE SUCH MEASURES AS THEY DEEM APPROPRIATE TO MITIGATE AGAINST THE ANY ADVERSE IMPACTS TO THE NATURAL ENVIRONMENT.  
3. THE CONTRACT SHALL RESTORE THE AFFECTED AREA TO ORIGINAL CONDITION OR BETTER, ALL TO THE SATISFACTION OF THE AUTHORITIES HAVING JURISDICTION.

THE SILTATION CONTROL PLAN IS INTENDED TO ASSIST THE CONTRACTOR IN THE LAYOUT AND CONSTRUCTION OF THE SILTATION CONTROL FEATURES ONLY. THIS DRAWING SHALL NOT BE USED FOR CONSTRUCTION OF SITE SERVICES.

**LEGEND**

- PROPOSED SILT FENCE
- STORM DRAIN INLET PROTECTION
- MAJOR OVERLAND FLOW DIRECTION
- EXISTING CONTOUR ELEVATION

**NOT FOR CONSTRUCTION**

**TOPOGRAPHIC INFORMATION**  
TOPOGRAPHIC INFORMATION PROVIDED BY J.D. BARNES LIMITED  
PROJECT No. 16-10-116-00, SURVEYS DATED NOVEMBER 30, 2017.  
PROJECT No. 16-10-116-00\_PH2, SURVEYS DATED SEPTEMBER 27, 2019.  
PROJECT No. 22-10-030-01, SURVEYS DATED JUNE 21, 2023.

**SITE PLAN INFORMATION**  
SITE PLAN PROVIDED BY Q4 ARCHITECTS, DATED ON JULY 9, 2025.

**ELEVATION NOTE**  
ELEVATIONS ARE GEODETIC AND ARE DERIVED FROM SITE BENCHMARK NCC CONTROL POINT 001196530229.  
ELEVATION = 86.12 m

9	S.L.M.	2025-08-26	8th SUBMISSION
8	S.L.M.	2025-08-14	7th SUBMISSION
7	S.L.M.	2025-07-15	6th SUBMISSION
6	S.L.M.	2025-06-10	5th SUBMISSION
5	S.L.M.	2025-05-28	4th SUBMISSION
4	S.L.M.	2025-05-13	3rd SUBMISSION
3	S.L.M.	2025-04-23	2nd SUBMISSION
2	S.L.M.	2025-04-02	DRAFT - ISSUED FOR ZONING BY-LAW AMENDMENT
No.	BY	DATE	DESCRIPTION

**Ottawa CITY OF OTTAWA**

PROJECT No. 24-1403

**S.L. MERRICK**  
10016822  
2025-08-26  
ON 24-1403

CAIVAN (ORLEANS VILLAGE 2) LTD.

ORLEANS VILLAGE  
PHASE 4

**DSEL**

120 Iber Road, Unit 103  
Stittsville, ON K2S 1E9  
Tel: (613) 836-0856  
Fax: (613) 836-7153  
www.DSEL.ca

**EROSION AND SEDIMENT CONTROL PLAN**  
STAGE 1

DRAWN BY:	C.P.B.	CHECKED BY:	S.L.M.	SHEET NO.
DESIGNED BY:	C.P.B.	CHECKED BY:	S.L.M.	23 OF 24
SCALE:	1:1000	DATE:	AUGUST 2024	

