


APPROVED
By Lily Xu at 12:20 pm, Dec 03, 2019

[Signature]

LILY XU, MCIP, RPP
(A) MANAGER, DEVELOPMENT REVIEW - SOUTH
PLANNING, INFRASTRUCTURE & ECONOMIC
DEVELOPMENT DEPARTMENT, CITY OF OTTAWA

- NOTES:**
1. SILT FENCE TO BE ERECTED PRIOR TO EARTH WORKS BEING COMMENCED. SILT FENCE TO BE MAINTAINED UNTIL VEGETATION IS ESTABLISHED OR UNTIL START OF SUBSEQUENT PHASE.
 2. STRAW BALE SEDIMENT TRAPS TO BE CONSTRUCTED IN EXISTING ROAD SIDE DITCHES. TRAPS TO REMAIN AND BE MAINTAINED UNTIL VEGETATION IS ESTABLISHED.
 3. SILT TRAPS TO BE PLACED AND MAINTAINED UNTIL SILT SACKS FULL. CATCHBASINS, GEOTEXTILE SILT SACK IN STREET CURBS TO REMAIN UNTIL ALL CURBS ARE CONSTRUCTED. GEOTEXTILE FABRIC IN RYOBARS TO REMAIN UNTIL VEGETATION IS ESTABLISHED. ALL CATCHBASINS TO BE REGULARLY INSPECTED AND CLEANED, AS NECESSARY, UNTIL SOD AND CURBS ARE CONSTRUCTED.
 4. WORKS NOTED ABOVE ARE TO BE INSTALLED, INSPECTED, MAINTAINED AND ULTIMATELY REMOVED BY SERVING CONTRACTOR.
 5. THIS IS A "LIVING DOCUMENT" AND MAY BE MODIFIED AT ANY TIME DURING THE PROPOSED CONTROL. MEASURES ARE INSUFFICIENT.

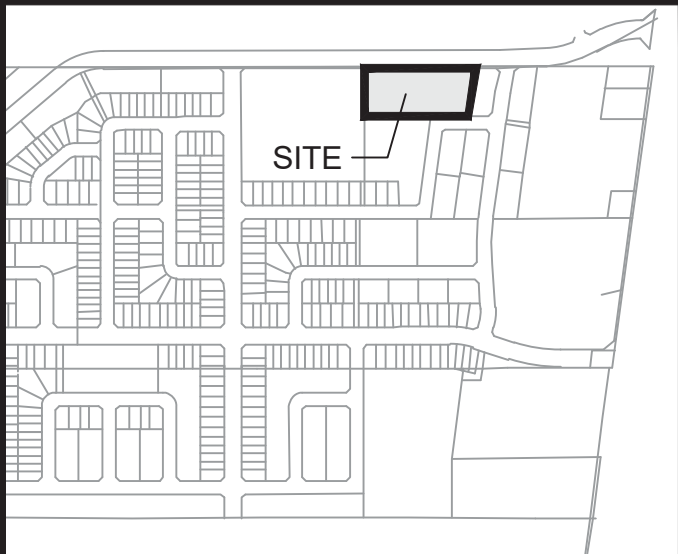







 **KEY PLAN**
N.T.S.

NOTES:

1. SEE DRAWING C-010 FOR ADDITIONAL DETAILS AND NOTES.
2. SITE BENCHMARK OBTAINED FROM LEGAL SURVEYOR ANNIS O'SULLIVAN VOLLEBEKK LTD.

LEGEND :

- | | |
|---|--|
|  | LIGHT DUTY SILT FENCE AS PER
OPSD-219.110 |
|  | SNOW FENCE |
|  | STRAW BALE CHECK DAM AS PER
OPSD-219.180 |
|  | ROCK CHECK DAM AS PER OPSD-219.210 |
|  | SILT SACK PLACED UNDER EXISTING CB
COVER |
|  | TEMPORARY MUD MAT 0.15m THICK 50mm
CLEAR STONE ON NON WOVEN FILTER
CLOTH |

14			
13			
12			
11			
10			
9			
8			
7			
6			
5			
4			
3			
2	REVISED AS PER CITY COMMENTS	DGY	19:07:19
1	ISSUED FOR SPA	DGY	19:04:01
REVISIONS		By	Date



IBI GROUP
400 – 333 Preston Street
Ottawa ON K1S 5N4 Canada
tel 613 225 1311 fax 613 225 9868
ibigroup.com

Project Title

BLOCK 225



Drawing Title

SEDIMENT AND EROSION CONTROL PLAN

Scale
1:500

Design RM/WZ	Date APRIL 2019
Drawn DPS/WZ	Checked DGY
Project No. 114312	Drawing No. 900
