


#### GENERAL NOTES

- CONTRACTOR TO INSTALL AND MAINTAIN SILT FENCE AND STRAW BALE CHECK DAMS AT LOCATIONS SHOWN OR AS DIRECTED BY THE ENGINEER.
- IF CONSTRUCTION IS INTERRUPTED AND/OR INACTIVITY EXCEEDS 30 DAYS, THEN STOCKPILED, STRIPPED OR EXPOSED AREAS MUST BE STABILIZED BY HYDROSEEDING AND ANY OTHER APPROPRIATE GEOTEXTILE MATERIAL, IF REQUIRED.
- REMOVAL OF ALL SILT FENCES AND STRAW BALE CHECK DAMS AT THE END OF CONSTRUCTION TO BE APPROVED BY THE ENGINEER AFTER THE SITE HAS STABILIZED.
- SILT FENCE TO OPSD 219.130 AND STRAW BALE CHECK DAM TO OPSD 219.180.
- CLEARING OF VEGETATION AND TREE COVER IS TO OCCUR OUTSIDE OF BIRD BREEDING SEASON AS RECOMMENDED BY THE CITY OF OTTAWA'S PROTOCOL FOR WILDLIFE PROTECTION DURING CONSTRUCTION (APRIL 15 - AUGUST 15).
- ALL SIDE SLOPES 3:1 OR GREATER ARE TO BE STABILIZED IMMEDIATELY WITH HYDROSEED (USING A NATIVE SEED MIX) UNLESS OTHERWISE NOTED. USE OF AN EROSION CONTROL BLANKET SUCH AS TERRAFIX S-100 (OR APPROVED EQUAL) IS RECOMMENDED IF CONSTRUCTION OCCURS OUTSIDE OF THE GROWING SEASON.

SITE

#### KEY PLAN - N.T.S.

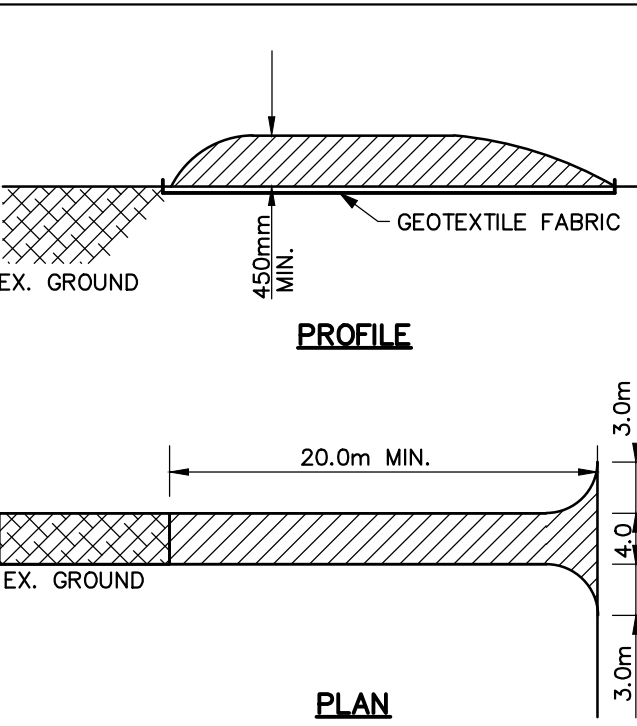

STONE SIZE - THE STONE PAD SHALL BE A MIN. 450mm THICK. USE 50mm STONE OR RECLAIMED CONCRETE EQUIVALENT FOR FIRST 10m FROM ADJACENT ROAD & 150mm STONE. FOR REMAINDER OF STONE PAD.

LENGTH - AS REQUIRED BUT NOT LESS THAN 20m.

WIDTH - 4m MIN. BUT NOT LESS THAN THE WIDTH AT POINTS WHERE INGRESS. AND EGRESS OCCURS. GEOTEXTILE FABRIC (TERRAFIX 270R OR EQUAL) WILL BE PLACED OVER THE ENTIRE AREA PRIOR TO PLACING STONE.

SURFACE WATER - ALL SURFACE WATER FLOWING OR DIRECTED TOWARD CONSTRUCTION ENTRANCES SHALL BE PIPED ACROSS THE ENTRANCE.


MAINTENANCE - THE CONTRACTOR SHALL MAINTAIN THE ENTRANCE IN A CONDITION WHICH WILL PREVENT TRACKING OR FLOWING OF SEDIMENT ONTO PUBLIC RIGHT-OF-WAY. THIS MAY REQUIRE PERIODIC DRESSING WITH ADDITIONAL STONE AS CONDITIONS DEMAND AND REPAIR AND/OR CLEANOUT OF ANY MEASURES USED TO TRAP SEDIMENT. ALL SEDIMENT SPILLED, DROPPED, WASHED OR TRACKED ONTO PUBLIC RIGHT-OF-WAY MUST BE REMOVED IMMEDIATELY BY THE CONTRACTOR. UPON OBSERVATION OF CONTINUOUS MUD TRACKING ONTO ADJACENT STREETS, THE STONE MAT IS TO BE FULLY REPLACED.

WASHING - WHEELS SHALL BE CLEANED TO REMOVE SEDIMENT PRIOR TO ENTRANCE ONTO PUBLIC RIGHT-OF-WAY. WHEN WASHING IS REQUIRED, IT SHALL BE DONE ON AN AREA STABILIZED WITH STONE AND WHICH DRAINS INTO AN APPROVED SEDIMENT TRAPPING DEVICE.

INSPECTION AND REQUIRED MAINTENANCE AFTER EACH RAIN SHALL BE PROVIDED BY THE CONTRACTOR.


#### STONE MUD MAT DETAIL

SCALE: N.T.S.

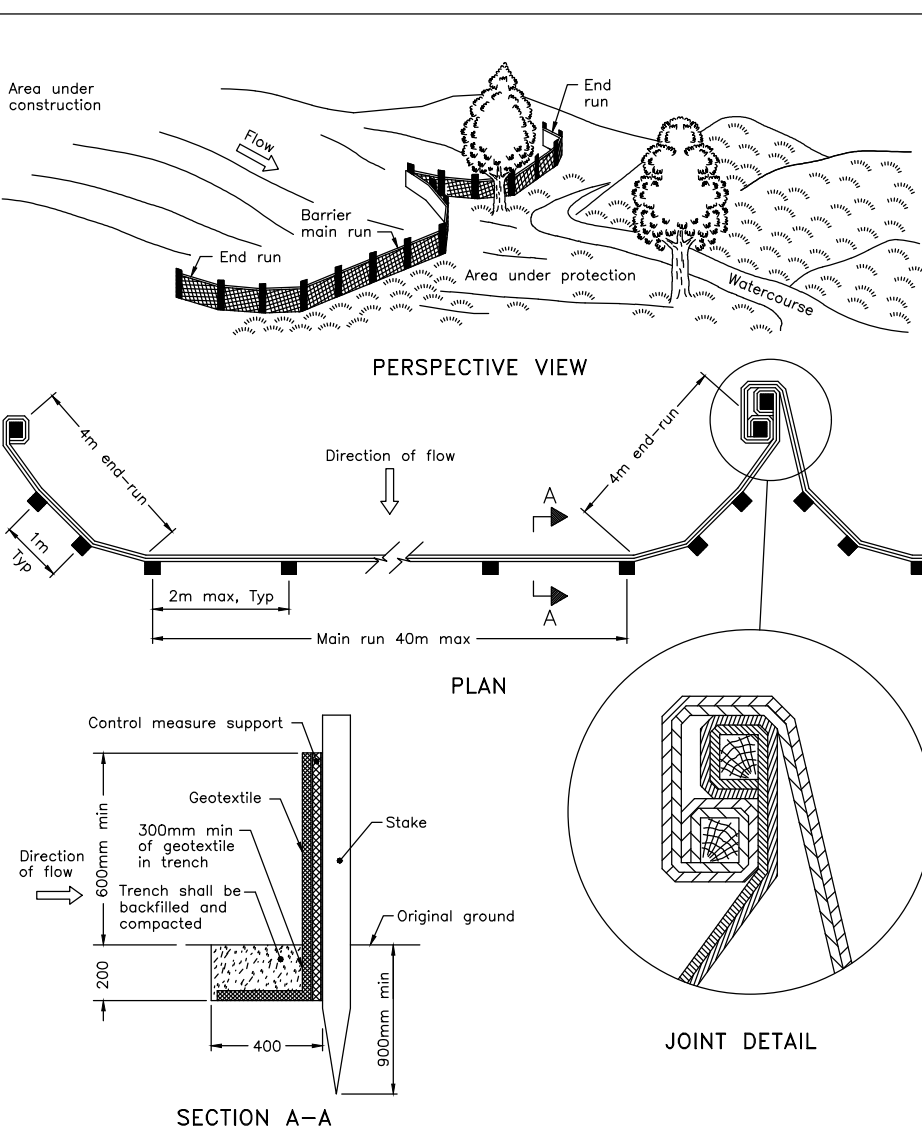

NOTE:  
A All dimensions are in millimetres unless otherwise shown.

ONTARIO PROVINCIAL STANDARD DRAWING	Nov 2015	Rev 2
HEAVY-DUTY SILT FENCE BARRIER	OPSD 219.130	

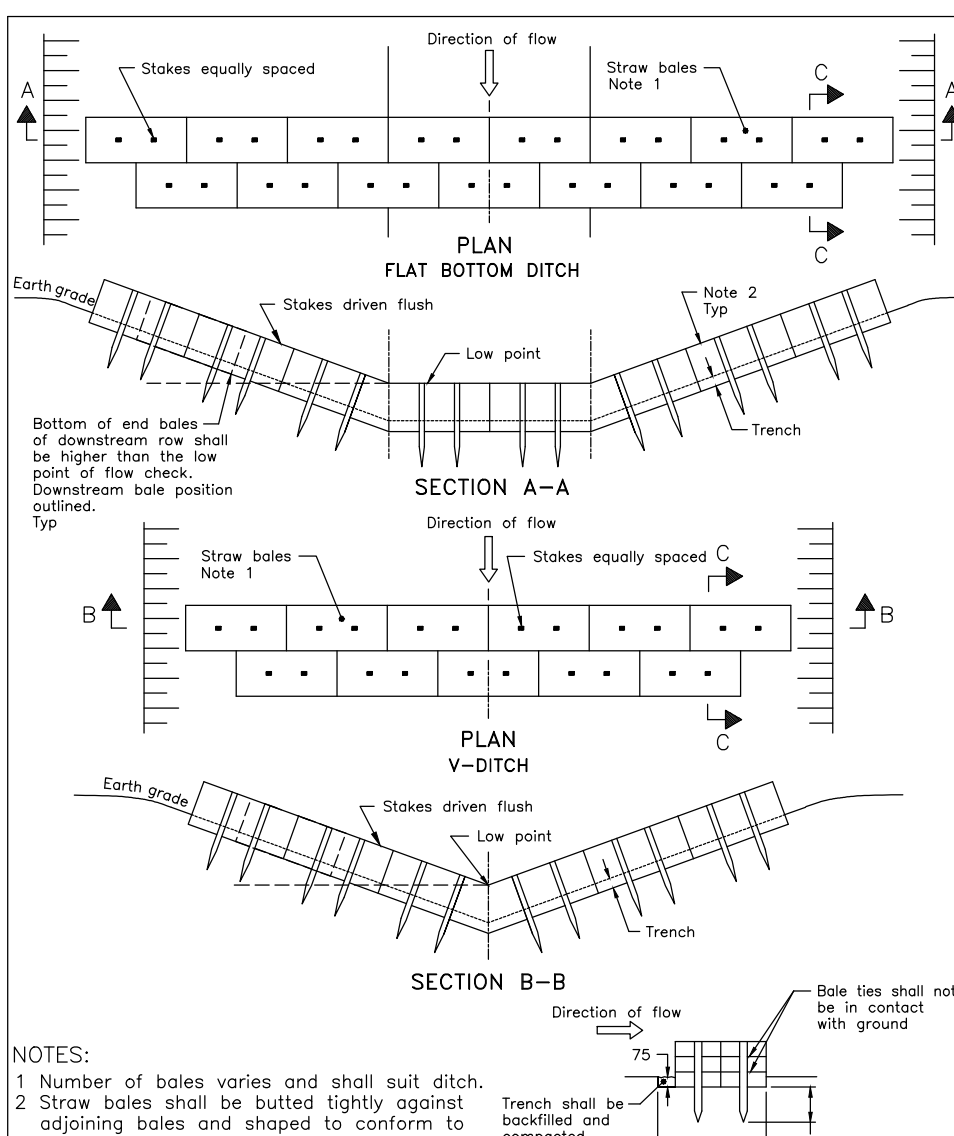

NOTES:  
1 Number of bales varies and shall suit ditch.  
2 Straw bales shall be butted tightly against adjoining bales and shaped to conform to the sides of the ditch to prevent water flow through barrier.  
A All dimensions are in millimetres unless otherwise shown.

ONTARIO PROVINCIAL STANDARD DRAWING	Nov 2015	Rev 2
STRAW BALE FLOW CHECK DAM	OPSD 219.180	

#### SCHEDULE OF CONSTRUCTION WORKS

- IMPLEMENTATION OF EROSION CONTROL MEASURES AS SPECIFIED ON THIS PLAN
- REMOVALS AS SPECIFIED ON THIS PLAN
- TOPSOIL STRIPPING AND STOCKPILING
- EXCAVATION OF THE DRY SWM FACILITY TO BE USED AS A TEMPORARY SETTLING BASIN DURING CONSTRUCTION. EXCAVATION OF SWALE TO INTERCEPT RUNOFF FROM THE CONSTRUCTION ZONE AND DIRECT IT TO THE SWM POND.
- EARTH EXCAVATION AND ROUGH GRADING THROUGH OUT THE SITE

#### LEGEND

- PROPERTY BOUNDARY
- BOTTOM OF SWALE AND FLOW DIRECTION
- EXISTING ELEVATION
- TEMPORARY STRAW BALE CHECK DAM AS PER OPSD 219.180
- HEAVY DUTY SILT FENCE AS PER OPSD 219.130

**DISCLAIMER AND COPYRIGHT**  
CONTRACTOR MUST VERIFY ALL DIMENSIONS AND BE RESPONSIBLE FOR SAME. ANY DISCREPANCIES MUST BE REPORTED TO THE ENGINEER BEFORE COMMENCING WORK. DRAWINGS ARE NOT TO BE SCALED.  
TATHAM ENGINEERING LIMITED CLAIMS COPYRIGHT TO THIS DRAWING WHICH MAY NOT BE USED FOR ANY PURPOSE OTHER THAN THAT PROVIDED IN THE CONTRACT BETWEEN THE OWNER/CLIENT AND THE ENGINEER WITHOUT THE EXPRESS CONSENT OF TATHAM ENGINEERING LIMITED.

TOPOGRAPHIC SURVEY COMPLETED BY ANNIS, O'SULLIVAN VOLLEBEKK LTD. ONTARIO LAND SURVEYOR, ON MAY 11, 2023.  
ELEVATION SHOWN ARE GEODETIC AND ARE REFERRED TO CGVD28 GEODETIC DATUM.  
TBM1: TOP OF PROPERTY IRON BAR LOCATED ON SOUTHEAST OF THE PROPERTY, ELEVATION 91.86.

No.	REVISION DESCRIPTION	DATE	ENGINEER STAMP
1.	ISSUED FOR APPROVAL	JAN 2025	



**1981 CENTURY RD. WEST**  
**CITY OF OTTAWA**  
**BUNSTAD CHRISTIAN CHURCH OTTAWA**  
  
**REMOVALS, SILTATION AND EROSION CONTROL PLAN**



DESIGN: HY	FILE: 523654	DWG:
DRAWN: HY	DATE: SEPT 2024	<b>SC-1</b>
CHECK: GC	SCALE: 1:400	
