



LILY XU, MCIP, RPP
MANAGER, DEVELOPMENT REVIEW SOUTH
PLANNING, INFRASTRUCTURE & ECONOMIC
DEVELOPMENT DEPARTMENT, CITY OF OTTAWA

APPROVED

By Lily Xu at 10:33 am, Jul 08, 2020

1. SILT FENCE TO BE ERECTED PRIOR TO EARTH WORKS BEING COMMENCED. SILT FENCE TO BE MAINTAINED UNTIL VEGETATION IS ESTABLISHED OR UNTIL START OF SUBSEQUENT PHASE.


2. STRAW BALE SEDIMENT TRAPS TO BE CONSTRUCTED IN EXISTING ROAD SIDE DITCHES. TRAPS TO REMAIN AND BE MAINTAINED UNTIL VEGETATION IS

3. SILT SACK TO BE PLACED AND MAINTAINED UNDER COVER OF ALL CATCHBASINS. GEOTEXTILE SILT SACK IN STREET CBs TO REMAIN UNTIL ALL CURBS ARE CONSTRUCTED. GEOTEXTILE FABRIC IN RYCBs TO REMAIN UNTIL VEGETATION IS ESTABLISHED. ALL CATCHBASINS TO BE REGULARLY INSPECTED AND CLEANED, AS NECESSARY, UNTIL SOD AND CURBS

4. WORKS NOTED ABOVE ARE TO BE INSTALLED,
INSPECTED, MAINTAINED AND ULTIMATELY REMOVED
BY SERVICING CONTRACTOR.

. THIS IS A "LIVING DOCUMENT" AND MAY BE MODIFIED IN THE EVENT THE PROPOSED CONTROL MEASURES ARE INSUFFICIENT.

6. THE CONTRACTOR SHALL IMPLEMENT BEST MANAGEMENT PRACTICES, TO PROVIDE FOR PROTECTION OF THE AREA DRAINAGE SYSTEM AND THE RECEIVING WATERCOURSE, DURING CONSTRUCTION ACTIVITIES. THE CONTRACTOR ACKNOWLEDGES THAT FAILURE TO IMPLEMENT APPROPRIATE EROSION AND SEDIMENT CONTROL MEASURES MAY BE SUBJECT TO PENALTIES IMPOSED BY ANY APPLICABLE REGULATORY AGENCY.

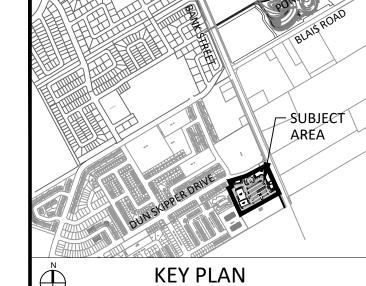

(NTS)

1. SEE DRAWING C-010 FOR ADDITIONAL DETAILS AND

2. SITE BENCHMARK TO BE OBTAINED FROM LEGAL SURVEYOR H.A. KEN SHIPMAN SURVEYING LTD.

LEGEND:

LIGHT DUTY SILT FENCE AS PER OPSD-219.110

SNOW FENCE

STRAW BALE CHECK DAM AS PER OPSD-219.180

ROCK CHECK DAM AS PER OPSD-219.210

SILT SACK PLACED UNDER EXISTING CB COVER

TEMPORARY MUD MAT 0.15m THICK 50mm
CLEAR STONE ON NON WOVEN FILTER
CLOTH


14			
13			
12			
11			
10			
9			
8			
7			
6			
5			
4			
3	REVISED AS PER CITY COMMENTS	JIM	2020:04:20
2	REVISED AS PER NEW SITE PLAN AND CITY COMMENTS	JIM	2019:10:11
1	ISSUED FOR SPA	JIM	2019:04:15
No.	REVISIONS	Ву	Date
			•


IBI

IBI GROUP 400 – 333 Preston Street Ottawa ON K1S 5N4 Canada tel 613 225 1311 fax 613 225 9868 ibigroup.com

Project Title

BANK STREET DEVELOPMENT 4836 BANK STREET





Drawing Title

EROSION AND SEDIMENTATION CONTROL PLAN

Scale 1 : 500

		<i>- - - - - - - - - -</i>
Design SEL	Date FEB. 2019	600-
Drawn DPS	Checked JIM	<u>-</u> 19-
Project No.	Drawing No.	12-
119351	900	D07-
